MTK

MEDIANTEK KILN · MANUFACTURING SOLUTIONS

DUT TEST REPORT

Report No. DUT-PASS-SN95308-000123-20261017-001213

1 · PRODUCT & TRACEABILITY

SERIAL NO.	**SN95308-000123**	PROJECT PART#	FRDM-MCXL255
CORE ID	95308	BATCH #	B20261016-01
STATION / OPERATOR	STN-01 / op01	REPORT TIME	2026-10-16T16:45:22

2 · TEST SUMMARY

10	10	0	PASS
ITEMS	PASS	FAIL	OVERALL

3 · TEST DETAIL

3.1 · IMPEDANCE (ICT)

#	TEST	MEASURED / DURATION	LOW	HIGH	UNIT	RESULT
1	Imp VDD_3V3	3.21	1.00		kΩ	PASS
2	Imp VDD_CPU	2.87	1.00		kΩ	PASS

3.2 · VOLTAGE (ICT)

#	TEST	MEASURED / DURATION	LOW	HIGH	UNIT	RESULT
1	VDD_3V3	3.302	3.20	3.40	V	PASS
2	VDD_CPU_0V8	0.801	0.78	0.82	V	PASS

3.3 · CLOCK (ICT)


#	TEST	MEASURED / DURATION	LOW	HIGH	UNIT	RESULT
1	CLK_24M	24.001	23.90	24.10	MHz	PASS
2	CLK_48M	47.998	47.80	48.20	MHz	PASS

3.5 · FLASH / FCT / RF & OTHER

#	TEST	MEASURED / DURATION	LOW	HIGH	UNIT	RESULT
1	Flash JLink FullChip	4.82				PASS
2	Init Instruments	0.82				PASS
3	WIFI RSSI	-42	-100	-55	dBm	PASS

3.4 · POWER RAILS UP SEQUENCE (DAQ AI)

Power Rails Up Sequence — PASS

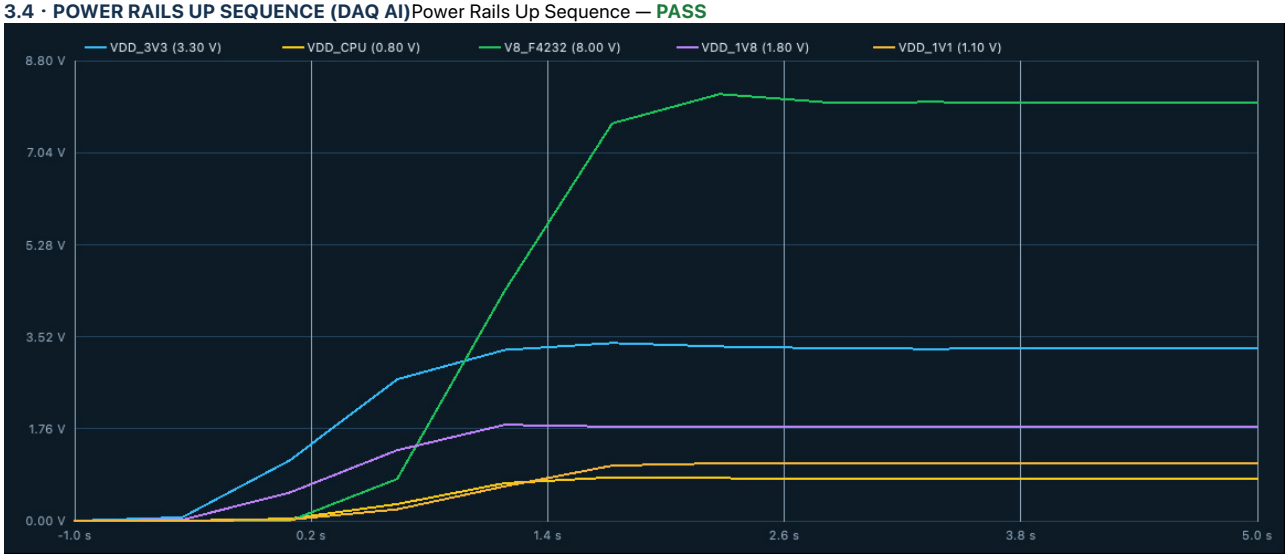

RAIL	NOMINAL V	FINAL V	RISE 10-90% s	PEAK V	OVERSHOOT	SETTLE ±5% s	RIPPLE P-P	NOTE
VDD_3V3	3.300	3.300	1.215	3.399	3.0%	1.182	132.0 mV	in regulation (±5%)
VDD_CPU	0.800	0.800	1.013	0.832	4.0%	1.727	34.4 mV	in regulation (±5%)
V8_F4232	8.000	8.000	1.023	8.160	2.0%	2.273	168.0 mV	in regulation (±5%)

VDD_1V8	1.800	1.800	1.225	1.836	2.0%	1.182	39.6 mV	in regulation (±5%)
VDD_1V1	1.100	1.100	1.303	1.100	0.0%	1.727	44.0 mV	in regulation (±5%)

4 · INSPECTION SEAL



5 · SIGN-OFF

TESTED BY	REVIEWED BY	AUTHORIZED BY MTK
op01		*MTK2A*

Electronically sealed by MTK GUI — this seal is bound to the report data by trace hash
sha256 · d2d0ec0a7a6e29dbc6a3fc506e7cbe4acdaa5851dae20693379ca8627e2365ae

Console Log

```
[16:38:02] DAQ973A connected
[16:45:20] All tests done
```
